



Activity ID	Activity Name	Duration	Start	Finish	2025										
					ch	16	23	30	06	13	20	27	04	11	8
					April				May						
<b>230022 CSU Dominguez Hills Student Housing Phase IV &amp; Dining Commons</b>															
<b>Project Milestones</b>															
PCM-3750	L2 Wall Pour Complete @ Student Housing	0		04-Apr-25	◆ L2 Wall Pour Complete @										
<b>Submittals, Approvals and Procurement</b>															
<b>Submittals</b>															
<b>Construction</b>															
<b>Site Preparation</b>															
<b>Mock Up</b>															
A1010	Mock -Up Construction	30	01-Jul-24 A	28-Mar-25	■ Mock -Up Construction										
A1020	Mock-Up review/Approval	10	31-Mar-25	11-Apr-25	▬ Mock-Up review/Appro										
<b>Construction - Student Residence</b>															
<b>Structure</b>															
<b>Level 1 (15k sq ft)</b>															
<b>Foundations</b>															
<b>Elevator Pit</b>															
STR-L1-1190	Waterproofing Elevator Walls	0	24-Mar-25	24-Mar-25	▮ Waterproofing Elevator Walls										
<b>Level 2 (15k sq ft)</b>															
<b>Columns Pour 2</b>															
STR-L2-1240	Form Columns - pour 2	2	24-Mar-25 A	25-Mar-25	■ Form Columns - pour 2										
STR-L2-1250	Place Concrete @ Columns - pour 2	1	26-Mar-25	26-Mar-25	▮ Place Concrete @ Columns - po										
STR-L2-1260	Strip/Clean Columns - pour 2	1	27-Mar-25	27-Mar-25	▮ Strip/Clean Columns - pour 2										
<b>Walls Pour 1</b>															
STR-L2-1310	Close Walls - pour 1	3	24-Mar-25 A	26-Mar-25	■ Close Walls - pour 1										
STR-L2-1320	Place Concrete @ Walls - pour 1	1	27-Mar-25	27-Mar-25	▮ Place Concrete @ Walls - pour										
STR-L2-1330	Strip/Clean Walls - pour 1	1	28-Mar-25	28-Mar-25	▮ Strip/Clean Walls -pour 1										



**CSUDH**  
**Student Housing & Dining Commons**  
**4 Week Look Ahead 25-Mar-25**



Activity ID	Activity Name	Duration	Start	Finish	2025										
					ch	16	23	30	06	13	20	27	04	11	8
					April				May						
<b>Walls Pour 2</b>															
STR-L2-1860	Walls Pour 2 - singleside walls	2	27-Mar-25	28-Mar-25											
STR-L2-1870	Walls Pour 2 - install rebar	2	28-Mar-25	31-Mar-25											
STR-L2-1880	Walls Pour 2 - install MEP	2	31-Mar-25	01-Apr-25											
STR-L2-1890	Walls Pour 2 - inspection	1	01-Apr-25	01-Apr-25											
STR-L2-1900	Walls Pour 2 - close walls	2	02-Apr-25	03-Apr-25											
STR-L2-1910	Walls Pour 2 - place concrete	1	04-Apr-25	04-Apr-25											
STR-L2-1920	Walls Pour 2 - strip/clean up	1	07-Apr-25	07-Apr-25											
<b>Level 3 (15k sq ft)</b>															
<b>Deck</b>															
STR-L3-1340	Form Raised Deck	6	03-Apr-25	10-Apr-25											
STR-L3-1350	MEPF Layout/Sleeves	3	09-Apr-25	11-Apr-25											
STR-L3-1360	Install Rebar (bottom & PT)	3	12-Apr-25	15-Apr-25											
STR-L3-1370	MEPF Rough-in	3	15-Apr-25	17-Apr-25											
STR-L3-1380	Install Rebar Top Mat	2	17-Apr-25	18-Apr-25											
STR-L3-1390	Formwork/Topwork	2	18-Apr-25	21-Apr-25											
STR-L3-1400	Inspection	1	21-Apr-25	21-Apr-25											
<b>Dining Facility (19k sq ft)</b>															
<b>Structure Dining Facility</b>															
<b>Grade Beams/Structural Steel</b>															
DH-STR-1300	Erect/Plumb Structural Steel	30	18-Feb-25 A	04-Apr-25											
DH-STR-1560	Plumb & Bolt	12	12-Mar-25 A	08-Apr-25											
DH-STR-1570	Weld	13	18-Mar-25 A	09-Apr-25											
DH-STR-1600	Install Cable Rail	3	25-Mar-25	27-Mar-25											
DH-STR-1580	Rebar Welding	10	25-Mar-25	07-Apr-25											

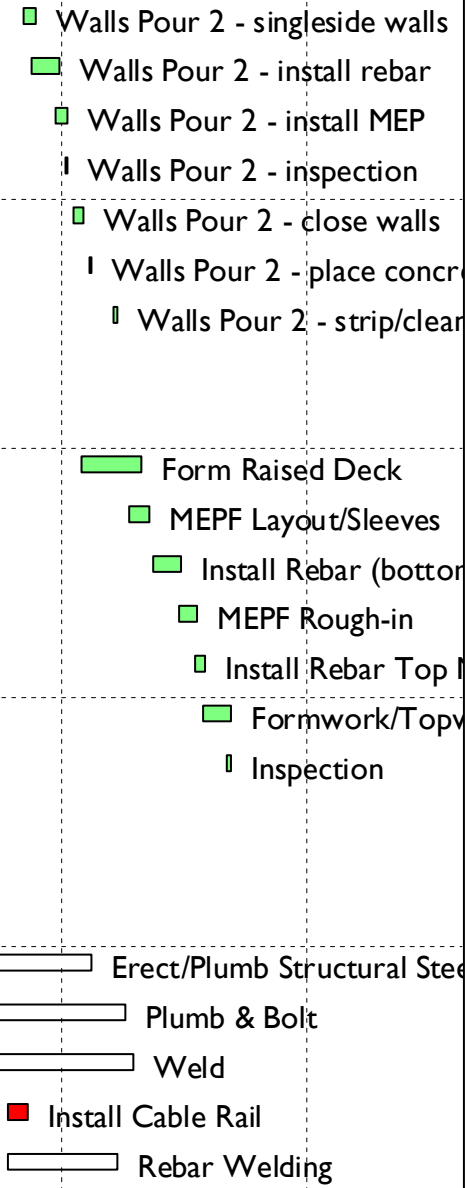

Run Date: 25-Mar-25  
Page 2 of 3



- Remaining Lev...
- Actual Level of...
- Actual Work
- Remaining Work
- Critical Remaini...

**CSUDH**  
**Student Housing & Dining Commons**  
**4 Week Look Ahead 25-Mar-25**

**CSUDH**  
CALIFORNIA STATE UNIVERSITY, DOMINGUEZ HILLS

**C.W. Driver**  
BUILDERS SINCE 1919

Activity ID	Activity Name	Duration	Start	Finish	2025															
					March			April				May								
					16	23	30	06	13	20	27	04	11	18						
<b>Metal Deck</b>																				
DH-STR-1060	Install/Weld Roof Deck - G to ZB Line	5	31-Mar-25	04-Apr-25																■ Install/Weld Roof Deck - G
DH-STR-1330	Mech. Enclosure Steel	5	07-Apr-25	11-Apr-25																■ Mech. Enclosure Steel
DH-STR-1280	Install/Weld Roof Deck - ZA to G Line	5	07-Apr-25	11-Apr-25																■ Install/Weld Roof Deck
<b>Slab on Grade</b>																				
DH-STR-1550	Underslab MEP Testing & Repair	5	07-Apr-25	11-Apr-25																■ Underslab MEP Testing
DH-STR-1470	SOG: In-Slab MEP/ Methane Vent Piping	5	14-Apr-25	18-Apr-25																■ SOG: In-Slab MEP/
DH-STR-1200	SOG: Fine Grade	2	21-Apr-25	22-Apr-25																■ SOG: Fine Grad
<b>Exteriors</b>																				
<b>Roof</b>																				
RF-DH-1130	Roof Electrical Rough	10	14-Apr-25	25-Apr-25																□ Roof Electrical
RF-DH-1140	Roof Mech Pipe Rough	10	14-Apr-25	25-Apr-25																□ Roof Mech Pip
<b>Summer Work Option B</b>																				

-  Remaining Lev...
-  Actual Level of...
-  Actual Work
-  Remaining Work
-  Critical Remaini...

**CSUDH**  
**Student Housing & Dining Commons**  
**4 Week Look Ahead 25-Mar-25**

